Financials | Changes | Coverage

Annual Financial Overview

DfT infrastructure projects · Annual reporting snapshots


2024-25 | 2025-26

Projects in scope
16

Forecast vs baseline
- 5.01%

Financial coverage
16 of 16 included observations have both baseline and forecast

Annual forecast variance by project (£m)

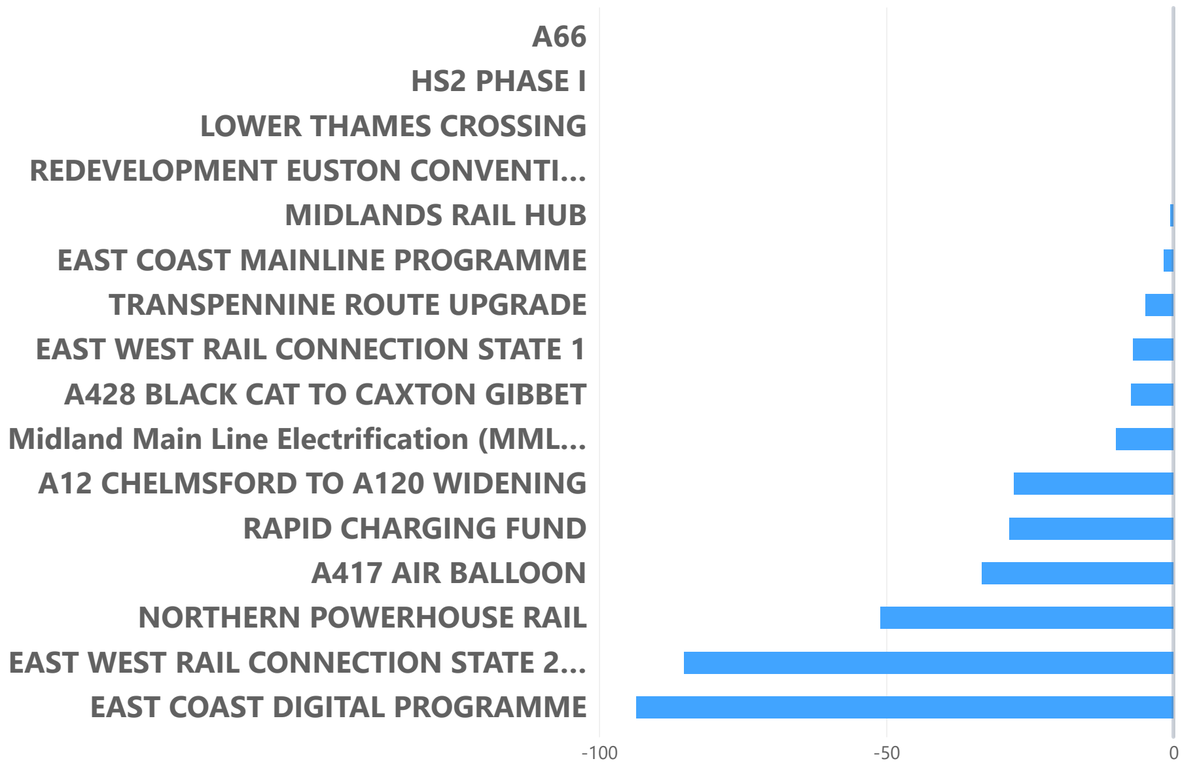

Project	Annual baseline (£m)	Annual forecast (£m)	Variance (£m)
TRANSPENNINE ROUTE UPGRADE	848.82	843.99	-4.83
REDEVELOPMENT EUSTON CONVENTIONAL STATION (RECS)	12.89	12.89	0.00
RAPID CHARGING FUND	33.00	4.50	-28.50
NORTHERN POWERHOUSE RAIL	131.61	80.59	-51.02
MIDLANDS RAIL HUB	5.13	4.65	-0.48
Midland Main Line Electrification (MMLE) Programme	41.00	31.00	-10.00
LOWER THAMES CROSSING	203.00	203.00	0.00
HS2 PHASE I	4,488.40	4,488.40	0.00
EAST WEST RAIL CONNECTION STATE 2 AND 3	175.29	90.15	-85.14
EAST WEST RAIL CONNECTION STATE 1	124.82	117.86	-6.96
EAST COAST MAINLINE PROGRAMME	25.65	24.00	-1.65
EAST COAST DIGITAL PROGRAMME	365.20	271.80	-93.40
A66	85.50	85.50	0.00

Data sources: https://www.gov.uk/government/publications/nista-major-projects-annual-report-2025-26

Financials | **Changes** | Coverage

Delivery Changes

31 March 2025 → 31 March 2026

Matched projects	Comparable schedules	Later published end date
13	5	1

Changes in Published End Dates

Project	March 2025 end date	March 2026 end date	Movement (days)
EAST COAST MAINLINE PROGRAMME	02/06/2026	03/05/2027	335
A417 AIR BALLOON	31/08/2027	31/08/2027	0
EAST COAST DIGITAL PROGRAMME	14/10/2030	14/10/2030	0
MIDLANDS RAIL HUB	31/12/2040	31/12/2040	0
TRANSPENNINE ROUTE UPGRADE	17/10/2041	17/10/2041	0

Delivery confidence - individual case

Project	March 2025 DCA	March 2026 DCA
EAST COAST DIGITAL PROGRAMME	AMBER	RED

Published end-date movements do not establish realised delays or causes. DCA comparison covers one eligible case.

Financials | Changes | Coverage

Reporting Coverage

Availability of published information and comparison limitations.

2024-25 | 2025-26

Published information availability

Reported Field	Available	Blank in source	Not yet available	Withheld
Annual baseline (£m)	16			
Annual forecast (£m)	16			
Annual variance commentary	16			
Benefits commentary	13			3
Cost commentary	11			5
Delivery confidence commentary	14			2
Department	16			
Evaluation plan (self-reported)	13			3
Expected benefits (£m)	11		1	4
External delivery confidence	6	8		2
Project category	16			
Project description	16			
Project end date	11		1	4
Project ID	16			
Project name	16			
Project start date	15			1
Published annual variance (%)	16			
Schedule commentary	13			3
Senior Responsible Owner	15			1
SRO delivery confidence	8	6		2
Whole-life cost (£m)	10		1	5

Projects not observed in the other release

Project	Status
A12 CHELMSFORD TO A120 WIDENING	Not observed in other release
Midland Main Line Electrification (MMLE) Programme	Not observed in other release
RAPID CHARGING FUND	Not observed in other release

--

Financial comparison

Figures are compared within each release. Cross-release monetary comparisons are disabled.

Schedule comparison

5 of 13 matched projects meet the schedule comparison rules.

DCA comparison

1 of 13 matched projects has verified assessment origin and comparable scope.
